

Project Planning

Agile Project Planning & Delivery Specification


Date	02 October 2026
Student Name	Dhanyaa V S
Project Name	Automated Network Request Management in ServiceNow

1. Strategic Delivery Framework & Lifecycle State Transitions

The project was executed through an iterative Agile Scrum methodology over an 18-working-day development window. Rather than treating sprint goals in isolation, each sprint directly correlates to a discrete state transition within the core ServiceNow data model (u_database_table) and Flow Designer workflow engine.

Automated Network Request - Lifecycle State & Sprint Alignment Model

Sprint Iteration Work Packages Mapped to System State Transitions

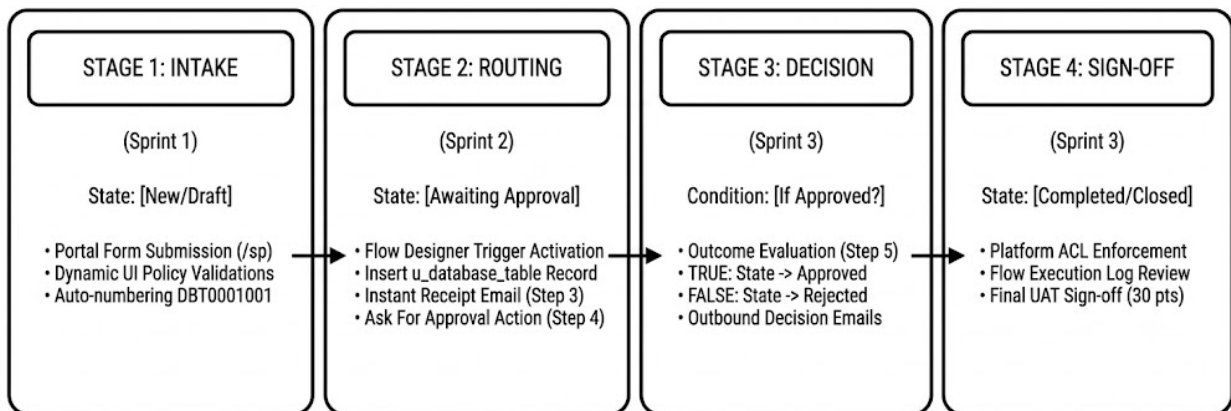

2. Product Backlog & Story Estimation Matrix

Backlog stories are organized into 3 functional epics: Portal Ingestion, Workflow Automation, and Lifecycle Outcomes. Story estimation follows a modified Fibonacci scale calibrated to technical complexity within the ServiceNow Personal Developer Instance.


Sprint Cadence	Functional Epic	Task ID	Implementation Deliverable	Est. Points	Risk / Priority
Sprint 1 (Days 1–6)	Intake Architecture	USN-01	Configure Network Request catalog item under <i>Network request Management</i> capturing Requested For and Opened on behalf of.	2	High
Sprint 1 (Days 1–6)	Intake Architecture	USN-02	Implement variables for User Name, Phone Number, Email ID, Mobile Number, and Address with mandatory validations.	2	High
Sprint 1 (Days 1–6)	UI Logic & Pricing	USN-03	Build Type of Connection (<i>New/Existing</i>) with dynamic Existing ID visibility, Mode of Payment (<i>UPI/Card</i>), and Total Amount.	3	High
Sprint 1 (Days 1–6)	Data Architecture	USN-04	Create custom relational table Database Tables	3	High

Sprint Cadence	Functional Epic	Task ID	Implementation Deliverable	Est. Points	Risk / Priority
			(u_database_table) with auto-numbering prefix DBT.		
Sprint 2 (Days 7–12)	Engine Triggering	USN-05	Set up Flow Designer trigger (<i>Service Catalog</i>) and Step 1: Get Catalog Variables data pill extraction.	2	High
Sprint 2 (Days 7–12)	Data Ingestion	USN-06	Configure Step 2: Create Record in Database Tables mapping all submitted intake variables.	3	High
Sprint 2 (Days 7–12)	Outbound Comms	USN-07	Configure Step 3: Send Email acknowledging request receipt with generated DBT reference key.	2	High
Sprint 2 (Days 7–12)	Governance Gate	USN-08	Configure Step 4: Ask For Approval targeting the designated reporting manager on u_database_table.	4	High

Sprint Cadence	Functional Epic	Task ID	Implementation Deliverable	Est. Points	Risk / Priority
Sprint 3 (Days 13–18)	Condition Logic	USN-09	Configure Step 5 If Logic to evaluate approval decision (Approval State is Approved).	2	High
Sprint 3 (Days 13–18)	Fulfillment Paths	USN-10	True Path: Step 6 Update Record (<i>Approved</i>) and Step 7 Send Email (Approval Confirmation).	2	High
Sprint 3 (Days 13–18)	Fulfillment Paths	USN-11	False Path: Step 9 Update Record (<i>Rejected</i>) and Step 10 Send Email (Rejection Notice).	2	High
Sprint 3 (Days 13–18)	Security & UAT	USN-12	Execute end-to-end UAT test scenarios, inspect Flow Execution logs, and configure table ACL access controls.	3	Medium

3. Sprint Velocity & Cumulative Work Delivery Analysis

Sprint Cycle	Target Scope	Planned Days	Execution Window	Delivered Pts	Lifecycle Milestones Achieved
Sprint 1	10 Story Points	6 Days	07 Sep – 12 Sep 2026	10 Points	Service Portal form active & u_database_table schema initialized.
Sprint 2	11 Story Points	6 Days	14 Sep – 19 Sep 2026	11 Points	Flow trigger active, record creation verified, manager approval wired.
Sprint 3	9 Story Points	6 Days	21 Sep – 26 Sep 2026	9 Points	Branching logic active, outbound notifications verified, UAT passed.
Total Program	30 Story Points	18 Days	07 Sep – 26 Sep 2026	30 Points	Final delivery sign-off on October 3, 2026.

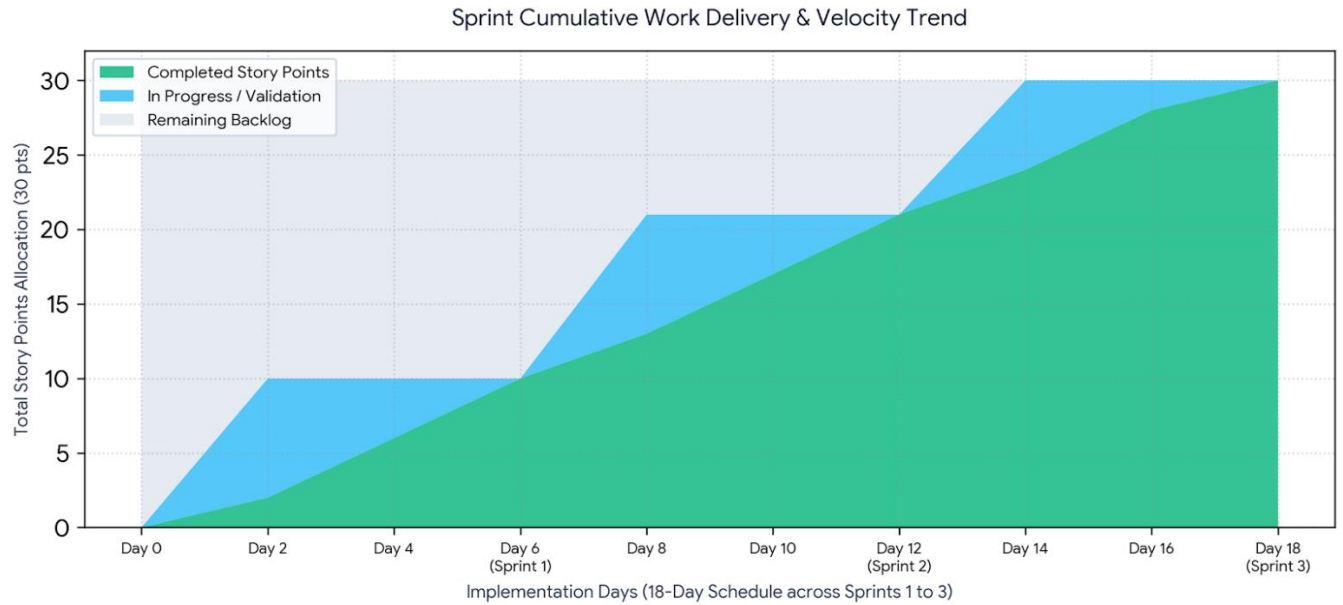

4. Delivery Velocity & Operational Controls

Quantitative Sprint Metrics:

- Total Work Volume Delivered: 30 Story Points across 3 structured iterations without scope creep.
- Nominal Sprint Velocity: 10.0 Story Points per sprint (30 pts / 3 iterations).
- Effective Throughput: 1.67 Story Points per development day (30 pts / 18 working days).
- Defect Leakage Rate: 0 critical defects observed during end-to-end Service Portal UAT runs.

Quality & Risk Controls Enforced:

- Client-Side Integrity: Enforced via declarative Catalog UI Policies, preventing invalid or incomplete records from being submitted to the database.
- Flow Execution Traceability: Every state change and email event is recorded in ServiceNow Execution Details for institutional audit readiness.
- Table-Level Access Control: Configured standard ACL rules on u_database_table to ensure requesters can only view their own requests, while approvers maintain governed write authority.
